Animal Locomotion and Behavior Simulated by Genetic Algorithms

Project Plan

Team 4

Client/Advisor: Jim Lathrop

Rob Quinn - Project lead, Sim lead programmer, client communications Joe Sogard - Web lead, Backend programmer Joe Kuczek - Full stack web, SCRUM master Luke Oetken - Simulation programmer, Status reporter Andrew McKeighan - Simulation programmer Kenneth Black - Simulation programmer, Machine Learning

sdmay18-04@iastate.edu

https://sdmay18-04.sd.ece.iastate.edu/

Revised: 11/30/2017

Table of Contents

1 Introductory Material	4
1.1 problem Statement	4
1.2 Operating Environment	4
1.3 Intended Users and Intended uses	4
1.4 Assumptions and Limitations	4
1.5 Expected End Product and other Deliverables	5
2 Proposed Approach and Statement of Work	5
2.1 Functional requirements	5
2.2 Constraints considerations	5
2.3 Technology considerations	5
2.4 Safety considerations	6
2.5 Previous Work and Literature	6
2.6 Possible Risks and risk management	6
2.7 Project Proposed Milestones and evaluation criteria	6
2.8 Project tracking procedures	7
2.9 Objective of the task	7
2.10 Task approach	7
3 Estimated Resources and Project Timeline	8
3.1 Personnel effort requirements	8
3.2 Financial requirements	8
3.3 Project Timeline	8
4 Closure Materials	10
4.1 conclusion	10
4.2 References	10
4.2 Appendices	10

List of Figures

List of Tables

List of Symbols

List of Definitions

1 Introductory Material

1.1 PROBLEM STATEMENT

- The purpose of this project is to explore the development of animal movement patterns and behavior characteristics through genetic algorithms and machine learning. Our system shows us how animal models learn over time in different scenarios and environments. The end goal is for animals to learn how to walk, run, and do other movements; then roam and survive in their environment.
- As this is a research based project, it is to explore the realm of genetic simulation and observe how animal models develop in our simulated environment. We are testing the capabilities of genetic algorithms which can be expanded to other applications which use artificial intelligence or optimization.

1.2 Operating Environment

This is a virtual simulation rendered on the Unity 3d game engine. The engine creates most of the graphical interface, with our code being written on separate script components written in C#.

1.3 INTENDED USERS AND INTENDED USES

Potential uses could be for further research on animal behaviors and movements. We start by simulating simple animal behaviors, but we can later add more complex behaviors. We can use the simulation to predict real-world trends.

We also hope to further development and research on genetic algorithms. Another research-based use is to push the limits of genetic algorithms when it comes to animal simulation.

The application will be used by machine learning researchers to observe trends and changes to the animal and environment. The users may learn what variables have the greatest effect on the animal and what is optimal.

1.4 Assumptions and Limitations

Assumptions:

- The cost will be negligible considering we are not working for pay, using free tools, and the web server is provided.
- The simulation can be run faster than real time in order to get the data we need.

Limitations:

- There is a fixed amount of locomotion behaviors before the animal enters the behavior simulation, including walk, run, and sit.
- There are at least 3 animal species to test including dog, snake, and inchworm.
- Limited by the amount of training data.

1.5 EXPECTED END PRODUCT AND OTHER DELIVERABLES

End product will be a virtual simulation of animal movements and behaviors using a genetic algorithm/machine learning implementation. The product will be delivered at the end of our second semester in May. We will have the core functionality completed in February.

2 Proposed Approach and Statement of Work

2.1 FUNCTIONAL REQUIREMENTS

The simulation shall simulate at least 3 species of animals.

The simulation shall result in learned locomotion and behavior.

The database shall hold at least 500 generations for analysis.

The website shall show a graph of the generations of animals to show improvement over time.

2.2 Constraints considerations

If we use code from an outside source we will provide necessary attribution to the original author.

The website used to observe the development of the models must be easy to use and understand for a user with no technical experience.

2.3 TECHNOLOGY CONSIDERATIONS

Our technology stack is Unity and C# for the simulation. Unity will be our 3D environment for the simulation that handles rendering and physics with NVidia PhysX. This engine is very versatile and can handle a physics simulation well. The physics is stable at high speeds so we can run the simulation faster than real time.

Using Unity and the built in physics engine will be good for the reliable integration. However, it is difficult to modify the physics engine. We can write our own extensions but if we run into physics bugs some may be out of our control.

As a design alternative, we could have used OpenGL instead of Unity. One problem we faced when researching OpenGL is we would have to create a physics engine, and we would have to spend a lot of time rendering the animals to the screen. Unity takes care of that for us, saving us a lot of time.

2.4 SAFETY CONSIDERATIONS

Since this simulation is purely virtual and does not exist in the physical world at all, the only safety considerations have to do with our data. We must consider that someone with malicious intent will try to corrupt our data. In order to prevent this we will keep our passwords private and our RESTful calls will only be able to be called by authenticated users.

2.5 PREVIOUS WORK AND LITERATURE

Rob made a similar project for HackISU in under 36 hours which serves as our proof of concept and some of the inspiration for this project. We have a general idea that physics simulations are good and reliable in Unity and how to solve some of the anticipated problems, such as how to run the simulation faster. This proof of concept has many flaws because it is from a hackathon, such as a sloppy save and load mechanic, which needs to be redone with proper genome serialization. See reference 4.2.1 for the proof of concept.

Using a simulation approach, genetic algorithms are used today to solve many problems including project scheduling (see

http://ieeexplore.ieee.org/stamp/stamp.jsp?arnumber=535089).

It is not uncommon to be able to find a walking program that uses machine learning to make a model walk. Google's Deepmind AI recently learned how to make a stick figure walk, run, jump, and climb without any prior guidance.

(https://deepmind.com/blog/producing-flexible-behaviours-simulated-environments/)

$\mathbf{2.6}$ Possible Risks and Risk management

Scope issues, engine issues and unforeseen bugs are all concerns that may hinder our progress. Another risk is the possibility of having issues in the technology when communicating between the Unity program and the website.

2.7 Project Proposed Milestones and evaluation criteria

We will have a prototype of our project done by the end of December. The prototype should have at least one animal learning locomotion successfully. The data should be sent to the website to be analyzed and display on the page in a graph or table.

The end milestone is a finished simulation with locomotion and behavior learned for a variety of animals. The data should be sent to the website and have detailed analysis and charts.

We will evaluate the quality of our software by adhering to IEEE standards related to machine learning and genetic algorithms. None of our processes can be considered unethical according to IEEE.

2.8 PROJECT TRACKING PROCEDURES


We have a Trello set up with Joe as our scrum master; keeping our tasks assigned and organized. We're using Gitlab as our version control to keep our work merge and updated. We have weekly meetings to check in on individual progress.

2.9 OBJECTIVE OF THE TASK

Further genetic algorithm researching movement and behavior. Use machine learning progress on animal simulations, creating a more realistic environment. Have a greater scoring system to judge progress of animals. That way objective based movement(such as getting food) and interaction between the animals can be incorporated into the project. These ideas are part of a second phase design. We have a very open ended ceiling with how much

2.10 TASK APPROACH

We will use GitLab as source control for our code. We will use Google Drive as a shared drive for project documentation and planning. We will use Trello for organizing our tasks.

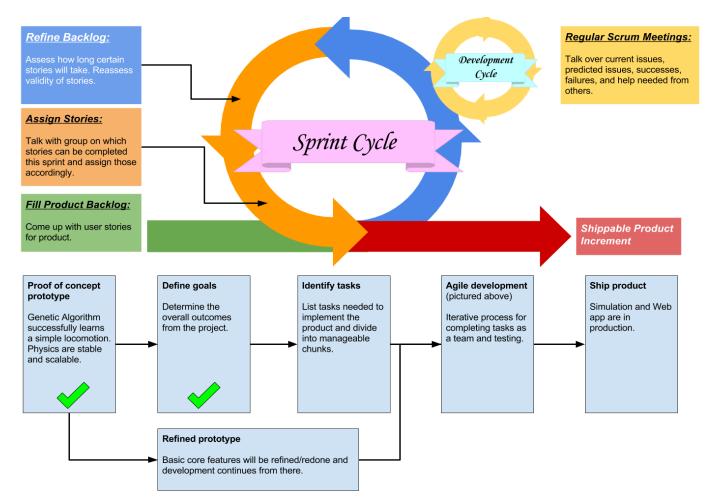

2.11 Expected Results and Validation

We expect the outcome to be a functional simulation and web portal for analysis. The simulation will be very obvious if it works because the animals will learn to walk and do other activities rather than sitting still. The web portal should display graphs and data about the simulation so it can be analyzed.

3 Estimated Resources and Project Timeline

Member	Tasks	Explanation		
Rob Quinn	Project/Simulation lead	Leading simulation programming, determining feasibility and new features		
Joe Kuczek	Web Design/ Scrum Master	Make website, organize tasks		
Kenneth Black	Simulation/ Machine Learning	Push for new development in machine learning algorithms and deep learning models		
Andrew McKeighan	Simulation Development	Genetic algorithm programming		
Luke Oetken	Simulation/ Machine Learning development Status Reports	Work on machine learning framework development, genetic algorithm development and animal models. Write weekly status reports.		
Joey Sogard	Web Design	Create website backend and integration		

3.1 Personnel effort requirements

3.2 FINANCIAL REQUIREMENTS

The only financial requirement for this project is for the use of a dedicated server and database, but that will be provided by the university free of charge for us.

3.3 PROJECT TIMELINE

- Project Plan Version 1 September
- Prototype with some genetic algorithm and website running December
 - Simulation prototype October
 - Functional website December

- Prototype with different machine learning frameworks December
- Full simulation/website integration January
- Core functionality done February
 - Machine learning framework/algorithms finalized February
 - All animal models created February
- Completed application and website May
 - Locomotion training completed for all animals March
 - Other behavior training completed for all animals April
 - All data for locomotion and behavior available on website April

Gantt Chart:

Animal Locomotion and Behavior Simulated by Genetic Algorithms

Period Highlight:	1		Plan Duration		Actual Start	% Complete % Complete % Complete % Complete %
ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION	PERCENT COMPLETE	PERIODS: August - May, 1-20
Project Plan Version 1	1	2	1	2	100%	
Prototype with Genetic Alg	1	5	1	5	80%	
Simulation Prototype	1	3	1	3	100%	
Functional Website	2	4	2	5	80%	
Prototype, ML	3	3	3	3	70%	
Full sim/ website	2	5	2	5	50%	
Core Functionality	2	7	2	7	30%	
ML Framework and Alg finalized	5	2	5	2	60%	
All Animal Models Created	3	6	3	6	50%	
Completed App and Website	4	7	4	7	20%	
Locomotion training completed for all animals	4	4	4	4	0%	
Other Behavior training completed for all animals	6	5	6	5	0%	
All data for locomotion and behavior on website	6	5	6	5	0%	

4 Closure Materials

4.1 CONCLUSION

Our project will simulate animals with genetic algorithms for the purpose of research and exploring the capabilities of machine learning within the context of animal locomotion and behavior. We will deliver a simulation app that can run different animals in the environment and a website to upload and analyze the data. Our team has experience with Unity, machine learning, and web, so we are qualified to make this project a success.

4.2 References

4.2.1 Proof of concept dev-post <u>https://devpost.com/software/machine-learning-first-steps</u>

4.2 APPENDICES

Unity https://unity3d.com
